

Lindenhurst Memorial Library

July 2021 Monthly Construction Report



Updated for August 17th, 2021, Board meeting



PARK EAST CONSTRUCTION

Prepared by Jim Burke & Robert Greenstein

Table of Contents

- **Section I** - Work Progress through the Month of July 2021 - Present
- **Section II** - Projected Work through the Month of August 2021
- **Section III** – Progress Photos for the Month of July 2021 - Present
- **Section IV** – Summary of Daily Manpower Reports July 2021 - Present

Work Progress - July 2021- Present

Renu Contracting and Restoration, Inc., Cooper Electric, KG Mechanical,
Hartcorn Plumbing and Heating Inc.

- Installation of temporary fence and gates
- Delivery of construction trailers
- Site Mark-outs
- ACM and lead removal
- Electric, HVAC, and Plumbing disconnects
- Interior and Exterior demolition
- Removal of stained - glass panels & packed for storage
- Temporary Electric Rough-in
- Commenced installation of 6" fire water service and RPZ unit
- Removal of trees along Lee Avenue
- Inspection of newly installed fire water service

Work Progress - July 2021- Present

Renu Contracting and Restoration, Inc., Cooper Electric, KG Mechanical,
 Hartcorn Plumbing and Heating Inc.

- Abatement of courtyard caulking
- Demolition of basement walls
- Provide power to fire water service
- Demolition of existing elevator and shaft
- Interior wall demolition
- Mezzanine exterior demolition
- Interior wall framing
- Install Gypsum boards, Tape, and Spackle
- RTU – 4 curb construction
- Continued west side site demolition
- Installation of curbs, RPZ footing, and dumpster footing

Proposed Work - August 2021

Renu Contracting and Restoration, Inc., Cooper Electric, KG Mechanical,
 Hartcorn Plumbing and Heating Inc.


- Relocate RTU – 4
- All trades continue Rough-in in Temporary Library
- Interior wall painting in Temporary Library
- Install interior doors and hardware in Temporary Library
- Complete exterior demolition
- Install temporary power to trailers (PSEG)
- Frame and pour walkway
- East side parking lot rough and final grading
- Installation of carpet tile

Lindenhurst Memorial Library




Before & After – 1st floor looking west

Lindenhurst Memorial Library

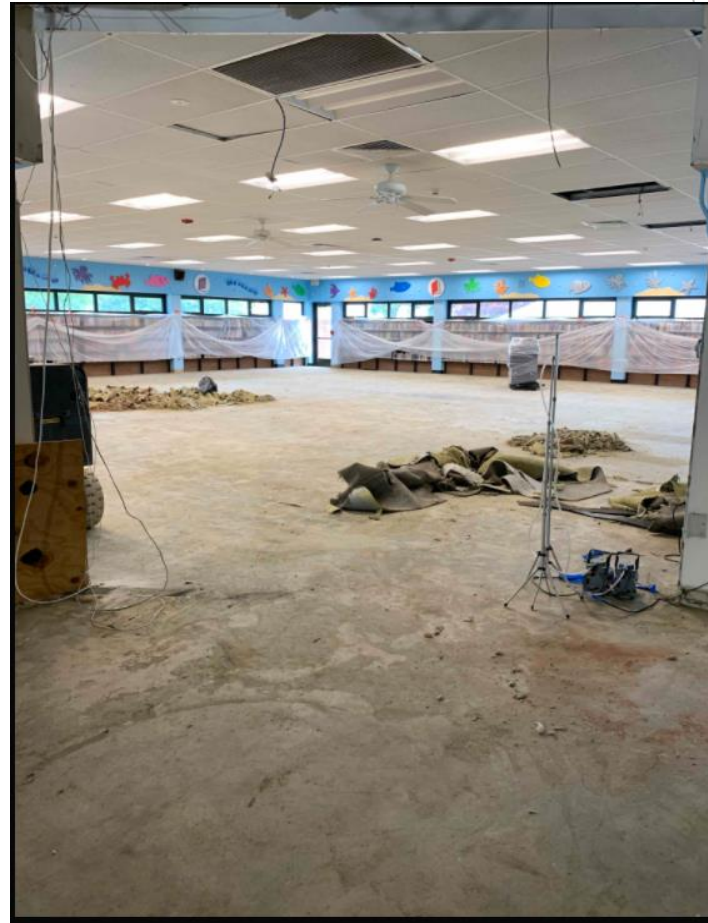


Before & After – Temporary Library

Lindenhurst Memorial Library

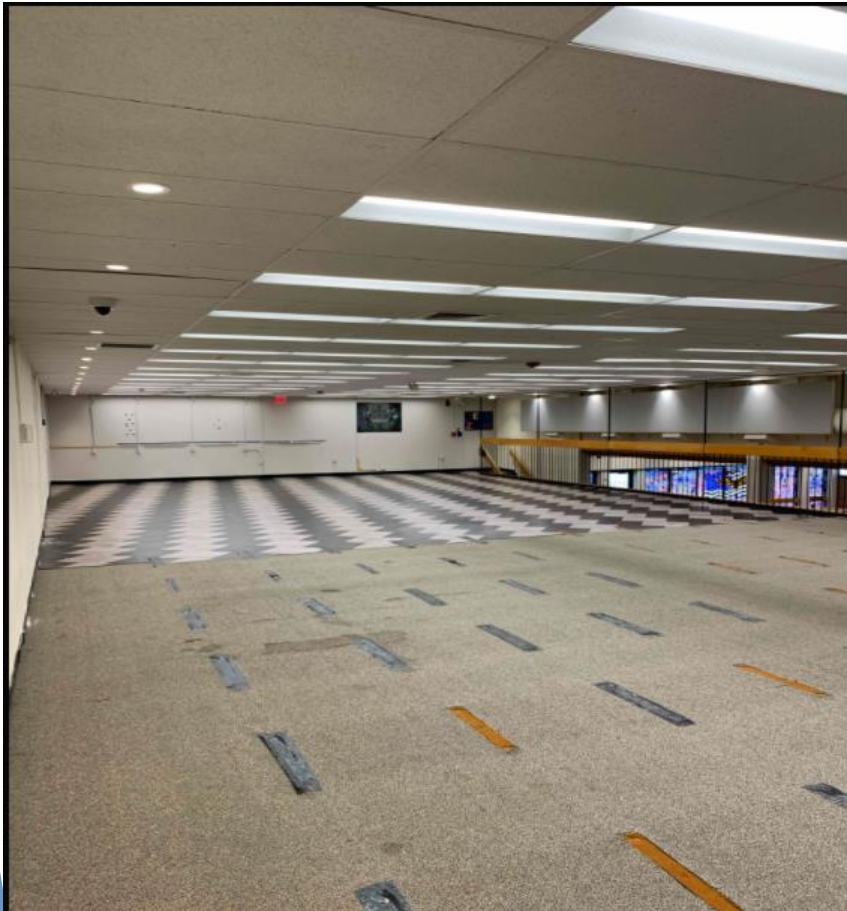

Before & After – Mezzanine

Lindenhurst Memorial Library

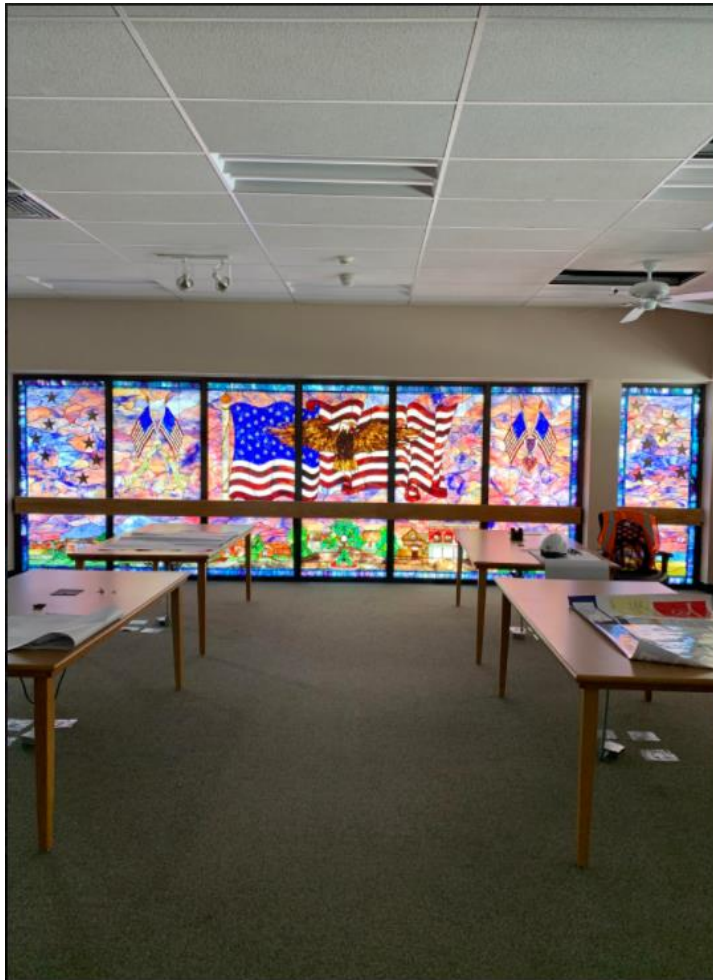

Before & After – Veterans Wall

Lindenhurst Memorial Library



Library West Elevation

Lindenhurst Memorial Library




Lindenhurst Memorial Library



Library Northwest elevation

Lindenhurst Memorial Library

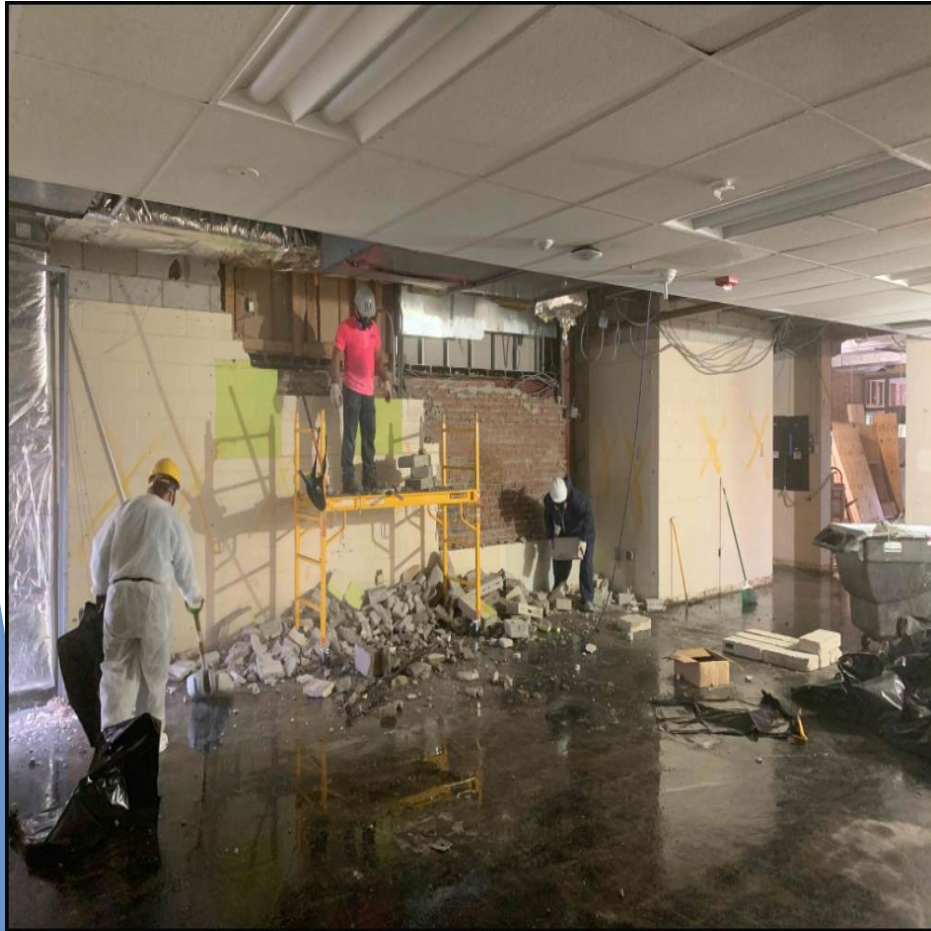

Before & After - Interior wall demolition

Lindenhurst Memorial Library



Before & After – Mezzanine demolition

Lindenhurst Memorial Library



Before & After – Childrens Room/Temp. Library

Lindenhurst Memorial Library




Curb installation


Lindenhurst Memorial Library





Manpower Report

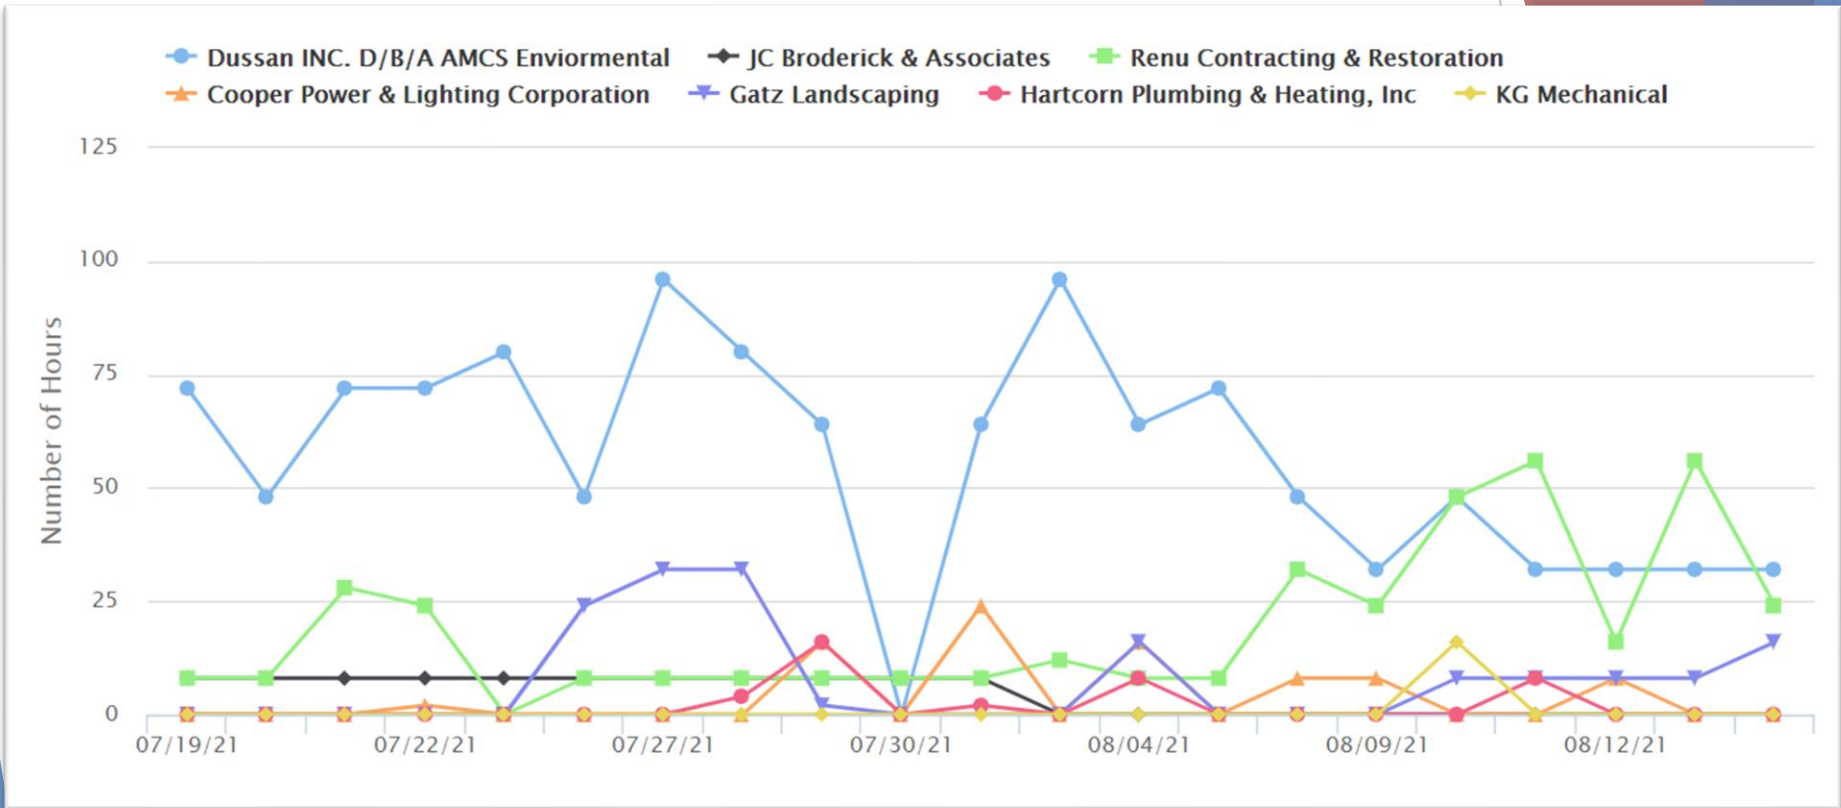



End of Report



PEC

LindenHurst Memorial Library Pre-construction June 23^{r,d}
